



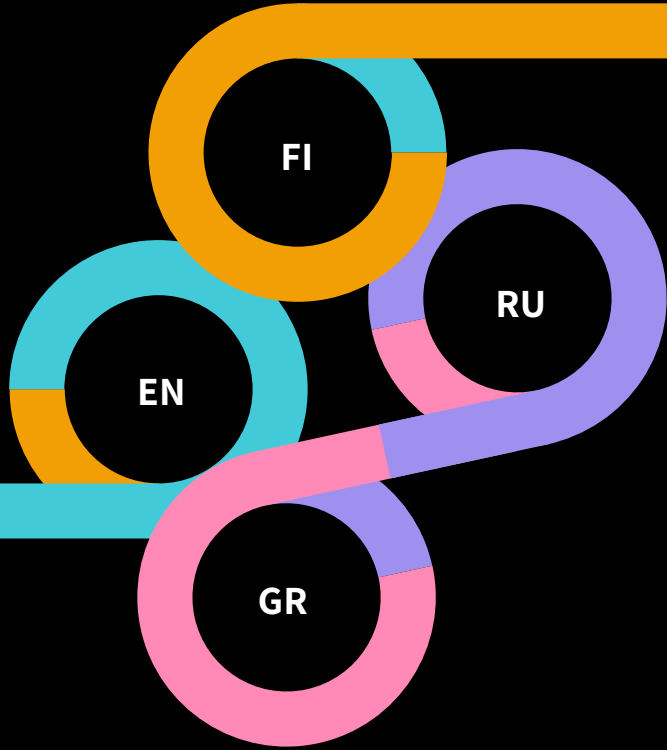


# Scrum Review for Sprint 5


# Table of Contents



# Scrum Process

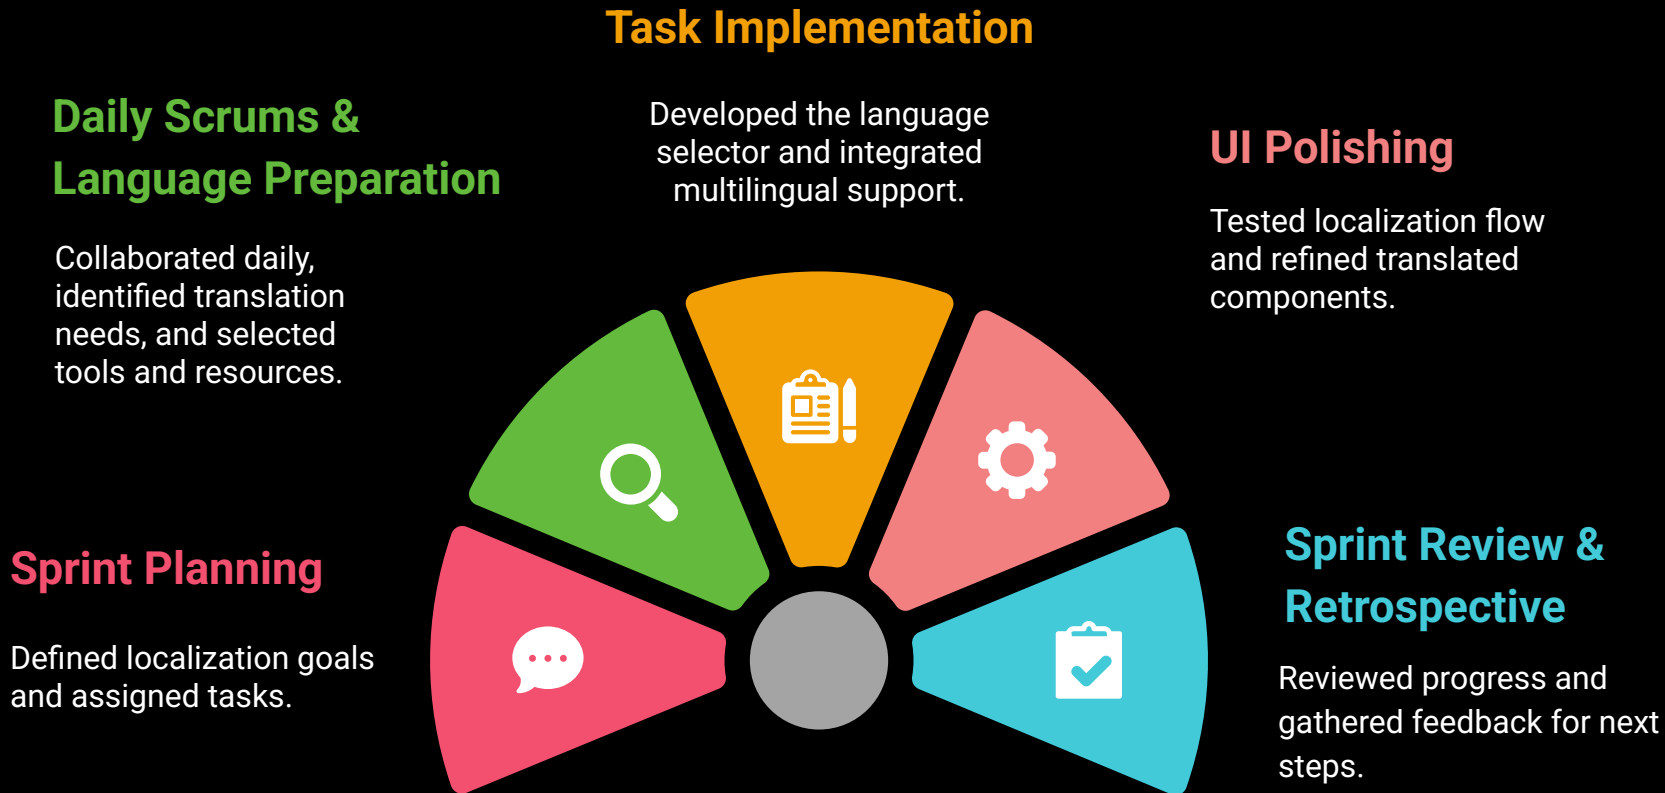

# Key Implementations

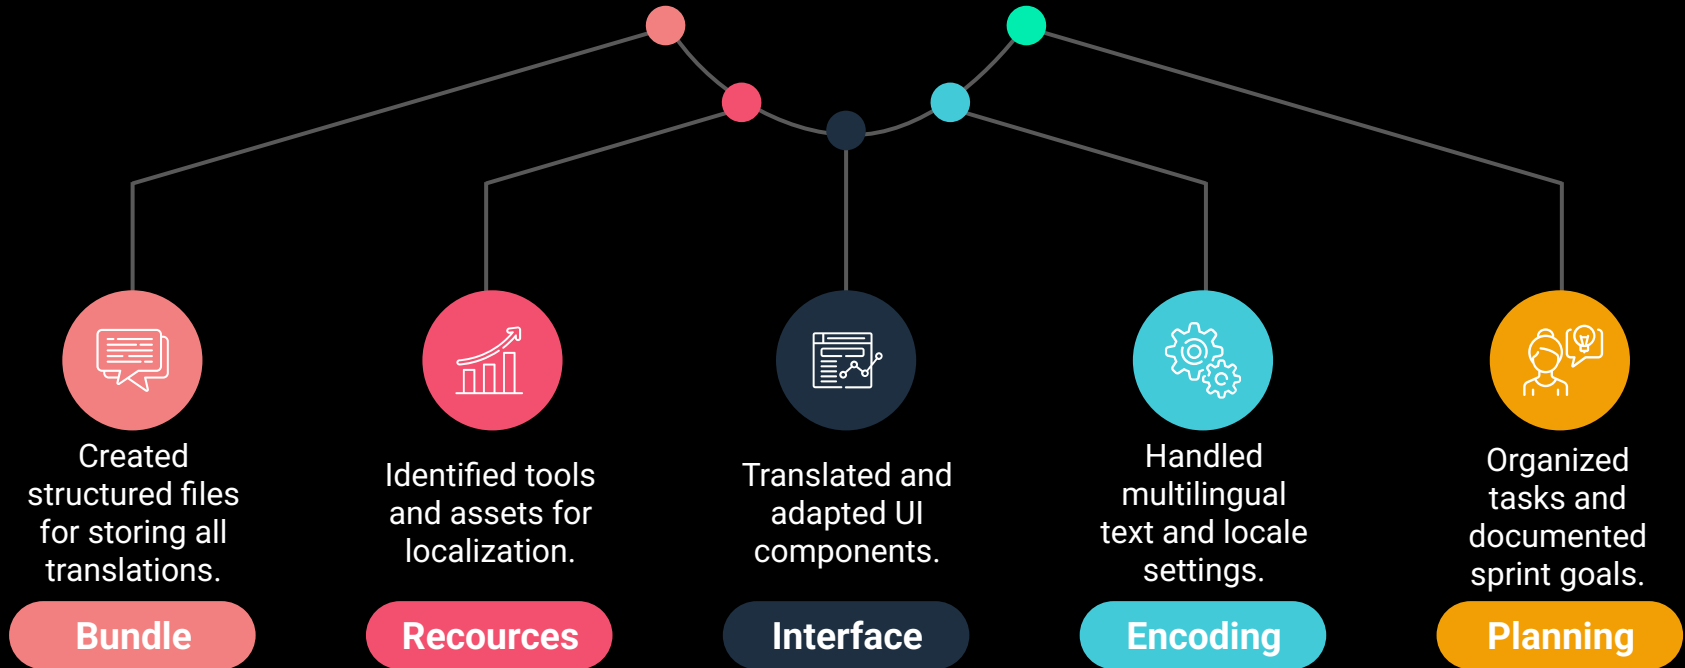



# Timeline

## Representation

Q Search timeline



Status category ▾

Epic ▾

### Sprints

- ☐ **SCRUM-5 Localization**
- ☐ **SCRUM-20** Create the language bundle **DONE**
- ☐ **SCRUM-21** Identification of Localization Resources **DONE**
- ☐ **SCRUM-6** Localize the User Interface **DONE**
- ☐ **SCRUM-24** Initial Sprint Planning and Sprint Review Re... **IN PROGRESS**
- ☐ **SCRUM-27** Sprint and Product Backlog Update **DONE**

MAR 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2

SCRUM Sprint 5



# Backlog

## Listing

| <input type="checkbox"/> | Type | # Key    | Summary                                             | Status      | Sprint         | Assignee       | Due date     |
|--------------------------|------|----------|-----------------------------------------------------|-------------|----------------|----------------|--------------|
| <input type="checkbox"/> | ▼    | SCRUM-5  | Localization                                        | TO DO       |                |                | Apr 1, 2025  |
| <input type="checkbox"/> | ▼    | SCRUM-20 | Create the language bundle                          | DONE        | SCRUM Sprint 5 |                | Mar 24, 2025 |
| <input type="checkbox"/> |      | SCRUM-22 | Create and fill sheets with translations            | DONE        | SCRUM Sprint 5 | Ivan Budanov   |              |
| <input type="checkbox"/> |      | SCRUM-23 | Transform sheets to the language bundles in the app | DONE        | SCRUM Sprint 5 | SA Saed Abukar |              |
| <input type="checkbox"/> |      | SCRUM-21 | Identification of Localization Resources            | DONE        | SCRUM Sprint 5 | Pavel Degterev | Mar 19, 2025 |
| <input type="checkbox"/> | ▼    | SCRUM-6  | Localize the User Interface                         | DONE        | SCRUM Sprint 5 |                | Mar 28, 2025 |
| <input type="checkbox"/> |      | SCRUM-31 | Integrate Resource Bundle into the Charts page      | DONE        | SCRUM Sprint 5 | VT Viet Tran   |              |
| <input type="checkbox"/> |      | SCRUM-19 | Adapt GPT Query Handling for Multilingual Responses | DONE        | SCRUM Sprint 5 | VT Viet Tran   |              |
| <input type="checkbox"/> |      | SCRUM-18 | Integrate the Resource Bundle into the Backend      | DONE        | SCRUM Sprint 5 | SA Saed Abukar |              |
| <input type="checkbox"/> |      | SCRUM-17 | Implement Language Selection Mechanism (Frontend)   | DONE        | SCRUM Sprint 5 | SA Saed Abukar |              |
| <input type="checkbox"/> | ▼    | SCRUM-24 | Initial Sprint Planning and Sprint Review Report    | IN PROGRESS | SCRUM Sprint 5 |                | Mar 31, 2025 |
| <input type="checkbox"/> |      | SCRUM-25 | Create and deliver Sprint planning                  | DONE        | SCRUM Sprint 5 | Ivan Budanov   |              |
| <input type="checkbox"/> |      | SCRUM-26 | Create and deliver Sprint review                    | IN PROGRESS | SCRUM Sprint 5 | Ivan Budanov   |              |
| <input type="checkbox"/> | ▼    | SCRUM-27 | Sprint and Product Backlog Update                   | DONE        | SCRUM Sprint 5 |                | Mar 21, 2025 |
| <input type="checkbox"/> |      | SCRUM-28 | Familiarize with Jira toolkit                       | DONE        | SCRUM Sprint 5 | Pavel Degterev |              |
| <input type="checkbox"/> |      | SCRUM-29 | Create the Backlog within our planning              | DONE        | SCRUM Sprint 5 | Pavel Degterev |              |



# All Tasks Achieved

- User Stories: 5
- User Story Points: 11

Projects / Stock Master

## SCRUM Sprint 5

Application Localization

Search

Epics

TO DO

+ Create issue

IN PROGRESS 1

Initial Sprint Planning and Sprint Review Report

LOCALIZATION 31 MAR

SCRUM-24

DONE 4 ✓

Create the language bundle

LOCALIZATION 24 MAR

SCRUM-20 ✓ 2

Identification of Localization Resources

LOCALIZATION 19 MAR

SCRUM-21 ✓ 1

Localize the User Interface

LOCALIZATION 28 MAR

SCRUM-6 ✓ 4

Sprint and Product Backlog Update

LOCALIZATION 21 MAR

SCRUM-27 ✓

POSTPONED

# Demo

Здравствуйете viet!

Выйти



GB

RU

GR



## Stockmaster3000

Войдите в свою  
учетную запись

Имя пользователя •

Пароль •



Войти

Еще нет аккаунта?

Зарегистрироваться





# Hours Contributed by Team

|           | Viet | Pavel | Ivan | Saed |
|-----------|------|-------|------|------|
| Tuesday   | 2    | 2     | 2    | 2    |
| Wednesday | 2    | 1     | 2    | -    |
| Thursday  | -    | -     | -    | -    |
| Friday    | -    | -     | 1    | -    |
| Saturday  | -    | 1     | -    | 1    |
| Sunday    | 2    | -     | -    | -    |
| Monday    | 1    | -     | -    | -    |
| Tuesday   | -    | -     | -    | -    |
| Wednesday | 2    | 1     | 1    | 6    |
| Thursday  | 3    | -     | 3    | 3    |
| Friday    | -    | -     | -    | -    |
| Saturday  | -    | -     | -    | 1    |
| Sunday    | 3    | -     | -    | -    |
| Monday    | 1    | 4     | 2    | -    |

|                |       |      |      |
|----------------|-------|------|------|
| Sprint 5 hours |       |      |      |
| Viet           | Pavel | Ivan | Saed |
| 16             | 9     | 11   | 13   |

# Daily Scrums



**Viet** 3/28/2025 12:37 AM  
Thursday 27.03.2025

What did I do today?

- Localization --> Inventory Chart Section

Any Problems?

- Trying to implement the Localization inside the cookie charts



**Saed** 3/27/2025 7:09 PM  
Thursday 27.03.2025

What did I do today?

- Added buttons, modified, styled and aligned (Localization header buttons)



**Buda** 3/27/2025 7:08 PM  
Thursday 27.03.2025

What did I do today?

- Added buttons
- Tried to result why flag buttons didn't work
- Resized layout

## Challenge Faced

- Working with the Vaadin framework's unique features
- Balancing time across multiple courses
- Adapting to new Jira tooling
